

# City of Lawton



## 2005 CIP Update

*October 2015*


**CITY OF LAWTON 2005 CIP SCHEDULE  
SALES TAX PROJECTS**

<i>Project</i>	<i>Project Status</i>
Street Reconstruction & Repairs	Project Complete
Water Distribution, Storage & SCADA	US 62 & I-44 Interchange Waterline Relocation - Reviewing Bids
SEWTP, Tower & Dist. Lines	Project Complete
Landfill Subtitle "D" Cells	Project Complete
Phase II Sewer Rehab Program	Project Complete
Accounting Hardware & Software	Project Complete
WWTP Ultraviolet System	Project Complete
NW 38th (Cache to Gore)	Project Complete
NW 67th (Rogers Lane to Cache)	Project Complete
SE 45th (Gore to Lee)	Design Complete\ODOT Project Agreement Approved\ ROW Acquisition Complete\Utility Relocations On-going
Meter Replacement Program	Project Complete
Numu Creek Drainage	Project Complete
Lake Dam Improvements (if funds available)	Pending Funding
Santa Fe Bridge	Project Complete

**CITY OF LAWTON AD VALOREM TAX PROJECTS**

<i>Project</i>	<i>Project Status</i>
Phase II Sewer Rehab Program	Project Complete
Cameron University Building (CETES)	Project Complete
Downtown Historic Preservation Project	Project Complete

# US 62 and I-44 Interchange Waterline Relocation Project # 2013-10

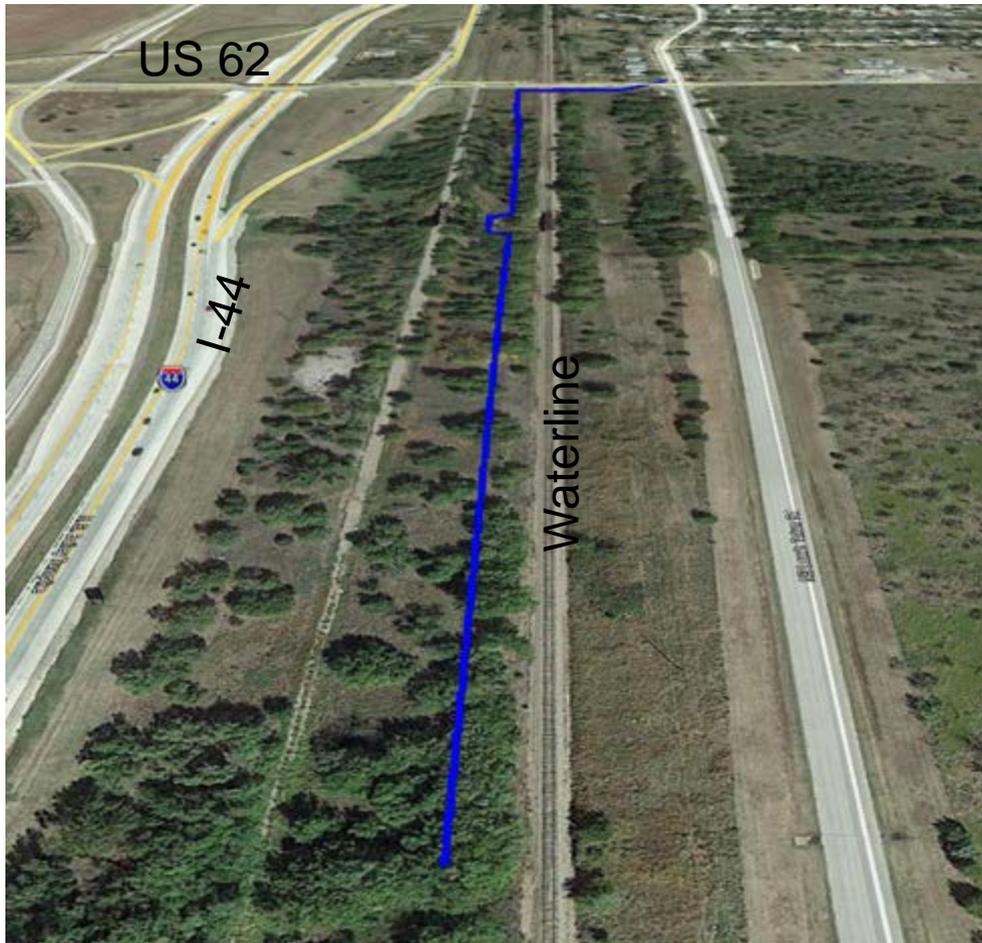

- ◆ In-House Engineering
- ◆ Council Executed a Right Of Way, Public Utility and Encroachment Agreement with ODOT at the February 11, 2014 Meeting.
- ◆ Relocating 3,000 L.F. of Waterline
- ◆ ODOT has Changed Alignment of SE Corner of Interchange Due to Right of Way Considerations.
- ◆ Council Approved Plans & Specs and Authorized Staff to Bid at the September 22, 2015 Meeting.
- ◆ Bids Opened October 27, 2015. Apparent Low Bid: \$460,678. Evaluating Bids.

# SE 45<sup>th</sup> Street Reconstruction Project # 2006-12 (Lee to Bell)



- ◆ Hendrick & Sons Co., Inc.
- ◆ Design Cost \$203,100
- ◆ Council Executed a Project Agreement with ODOT for 80% Construction Costs up to a Maximum of \$6.0 Million at the January 22, 2013 Meeting.



- ◆ Council Awarded Contract in the Amount of \$2,540,000 to Southwest Water Works LLC for Relocation of Water & Sewer lines October 27, 2015
- ◆ Utility Relocations On-going
- ◆ Anticipate Spring 2016 for ODOT Bid Letting.

# City of Lawton



## 2008 CIP Update

*October 2015*

**CITY OF LAWTON 2008 CIP SCHEDULE**

<b>Project Description</b>	<b>Project Status</b>
<b>STREETS</b>	
Ward One	All Projects Complete
Ward Two	Identified Overlay Projects Complete
Ward Three	All Projects Complete
Ward Four	Overlay Projects Under Construction
Ward Five	Overlay Projects Complete; Reconstruction Projects Under Construction
Ward Six	Identified Overlay Projects Complete
Goodyear/Cache Road Intersection	Project Complete
Ward Seven	Overlay Projects Complete; Reconstruction Projects Under Construction
Ward Eight	Identified Overlay Projects Complete
Citywide Local Residential Street Reconstruction (Design)	Project Complete
Purchase Asphalt Paving Machine	Project Complete
BRAC & Existing CIP Projects	NW 67th (Cache to Rogers Ln) Complete
	NW 2nd (Gore to Columbia) Complete
	SW 2nd (Gore to "C" Ave.) Complete
Residential Street Designs	Projects Complete
Rogers Lane (I-44 to Flower Mound)	Project Divided Into 2 Phases/ODOT Funding Received; Phase 1. ODOT NEPA Study ongoing on both Phases
<b>WATERLINE IMPROVEMENTS</b>	
Low Flow Hydrant Project #1	Project Complete
Low Flow Hydrant Project #2	Project Complete
Low Flow Hydrant Project #3	Project Complete
Low Flow Hydrant Project #4	Funding Used For Projects 1,2 & 3; Project Complete
Enterprise Car Rental F.H.	Project Complete
Western Hills Christian Church F.H.	Project Complete
Lawton Country Club Waterline	Project Complete
2315 NW Sheridan Road FH	Project Complete
5510 NW Cache Road FH	Project Complete
Cache Road Square FH's	Project Complete
Los Arroyos FH	Project Complete
2014 Waterline Replacement Project 2014-8	Under Construction
67th Street Chlorine Pump Station	Under Construction
<b>SEWERLINE IMPROVEMENTS</b>	
Nine Mile Creek Sewer Line (Design & ROW Acquisition)	Final Design Complete/ROW Acquisition On-going
<b>SEWER REHAB PROGRAM</b>	
Phase II Sewer Rehab Projects	Phase II Projects Complete

# City Wide Street Reconstruction



SE 45<sup>th</sup> Street (Ellsworth to Brown) – Ward 4




SE 45<sup>th</sup> Street – Asphalt Complete

# Rogers Lane Roadway Project (Flower Mound to I-44)



- ◆ Garver Engineers
- ◆ Design Cost \$865,600
- ◆ Design – Plans/Specifications:  
5 – Lane Roadway

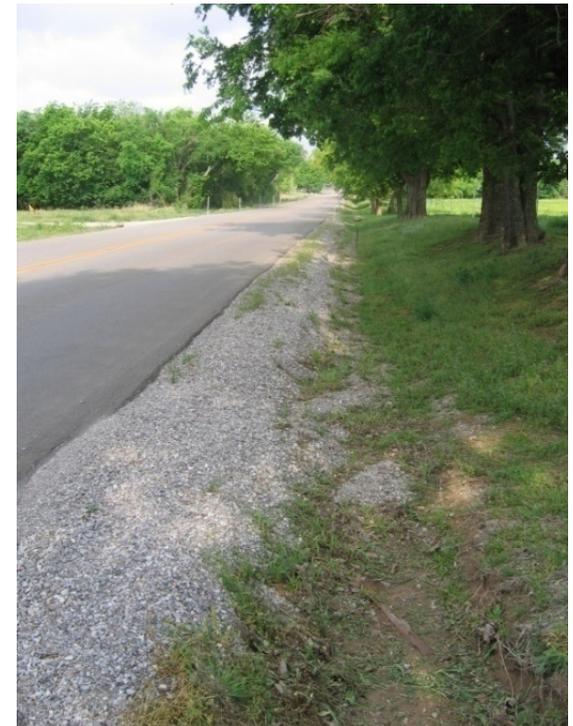

- ◆ Project Split Into Two (One Mile) Sections
- ◆ Phase 1 Design On-going
- ◆ Council Executed a Project Agreement with ODOT for 75% Construction Costs up to a Maximum of \$5.8 Million at the April 23, 2013 Meeting.
- ◆ ODOT Submitted Draft Environmental Clearance Document to City for Review and Comment

# 2014 Waterline Replacement Phase 1

## Project # 2014-8



- ◆ Southwest Water Works, LLC
- ◆ Construction Cost \$4,347,618
- ◆ Council Awarded a Construction Contract at the December 16, 2014 Meeting.

- ◆ Approximately 4.8 Miles of Waterline Replacement from Gore Blvd. on the North to Lee Blvd. on the South and from 13<sup>th</sup> Street on the West to 3<sup>rd</sup> Street on the East
- ◆ Installing East/West Waterlines between Gore Blvd and "F" Avenue.




# NW 67<sup>th</sup> Street Chlorine Injection Pump Station Project



- ◆ Council Approved a Design/Build Contract at the December 9, 2014 Meeting.

- ◆ Meridian Contracting, Inc.
- ◆ Design/Build Cost \$800,000
- ◆ Notice to Proceed: January 26, 2015
- ◆ Construction On-going
- ◆ System Control Panels and Overhead Doors for Building Remain



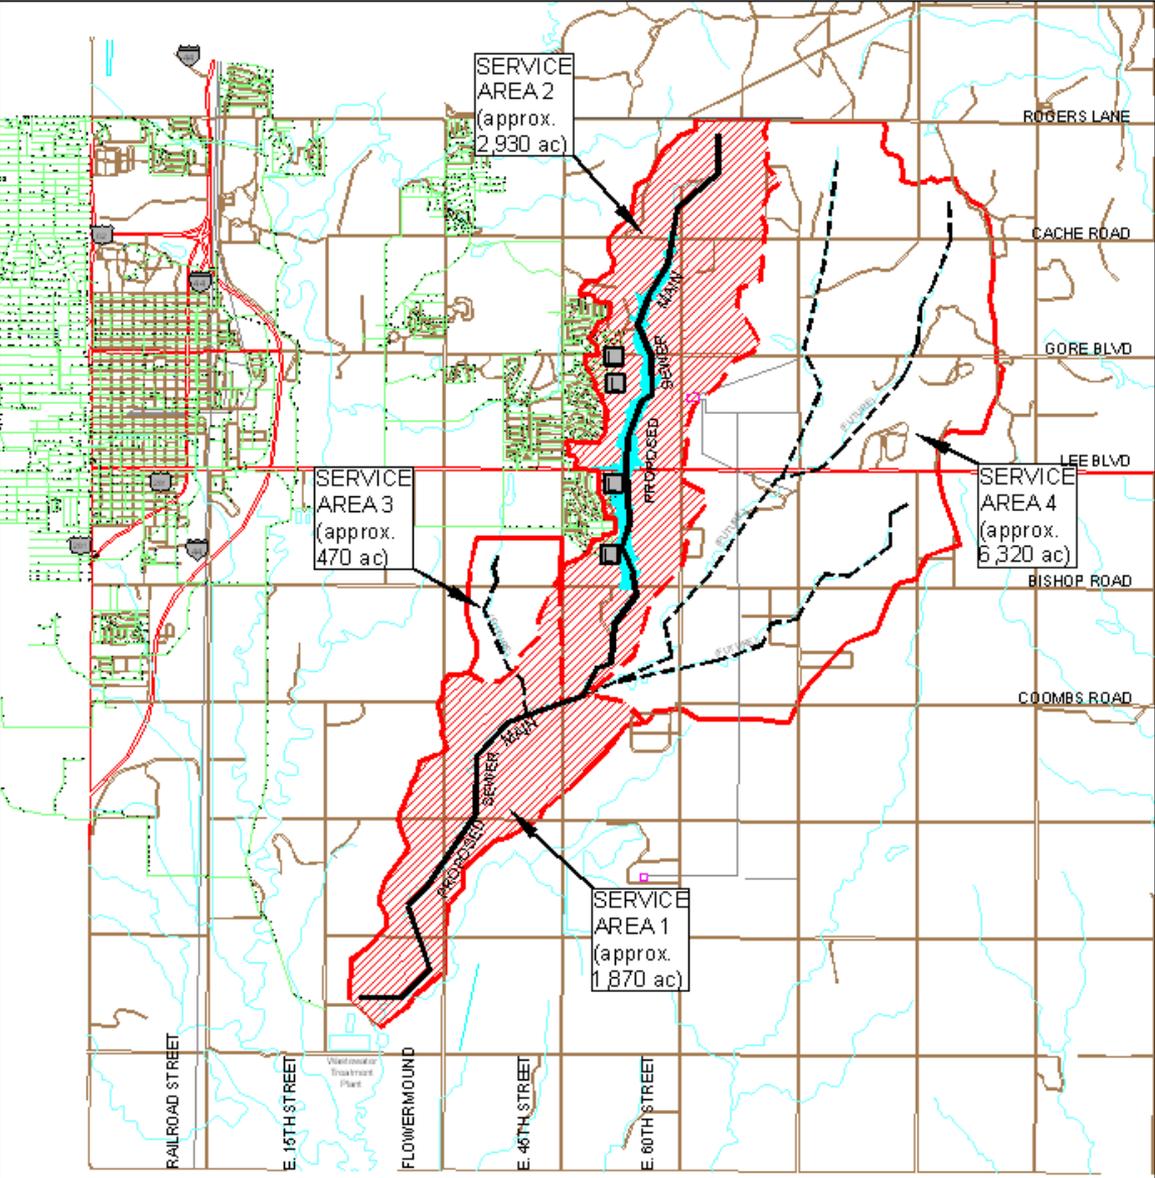

NTS

NINE MILE CREEK SEWER  
 LINE PROJECT #2008-2  
 PHASE I  
 WWTP TO BISHOP RD.

- ◆ PSA-Dewberry, Inc.
- ◆ Design Cost \$226,740
- ◆ Council Awarded Design Contract at the October 14, 2008 Meeting.
- ◆ Right Of Way Acquisition Process On-going
- ◆ Acquisition of Phase 1 Complete
- ◆ Acquiring Phase 2 Properties for Construction. One Parcel Remains.
- ◆ Ready to Bid Phase I with 2016 CIP Package

# City of Lawton



## 2012 CIP Update

*October 2015*

**CITY OF LAWTON 2012 CIP SCHEDULE**

**SALES TAX FUNDED PROJECTS**

<b>PROJECT TYPE &amp; LOCATION</b>	<b>PROJECT STATUS</b>
<b>Mandatory Project Improvements</b>	
Phase III - Sewer Rehabilitation Program	Under Construction (27% Complete); Working on Damage from May Floods
Work Package # 2 @ WWTP	Under Construction (95% Complete)
Landfill Cells 6 & 7 and Land Purchase	Begin Design in January 2020
MPWTP Water Clearwell	Project Substantially Complete
City Car & Truck Wash Facility	Project Complete
<b>Arterial Roadway &amp; Bridge Improvements</b>	
SE 45th St. (Lee Blvd. to Bell Ave.)	Utility Relocations Ongoing (Joint City & ODOT Project)
SW 2nd St. (Gore Blvd. to "C" Ave.)	Project Complete
NW 2nd St. (Columbia to Ferris Ave.)	Council Approved Plans and Specifications; Ready to Bid
SW 52nd St. (Gore to RR Tracks)	ROW Acquisition On-going
Citywide Mill & Overlay Program - Project #1	NW Cache (52nd-Hunter) ; W Gore (Sheridan-40th) Project Complete
Citywide Mill & Overlay Program - Project #2	W 112th St. (Lee to RR Track) & Lee (112th to 0.3 miles East) Project Complete
Citywide Mill & Overlay Program - Project #3	W Gore (Lawton Country Club to 67th) Project Complete
Citywide Mill & Overlay Program - Project #4	W 112th St.(RR Track to Cache Rd.) Project Complete
Citywide Mill & Overlay Program - Project #5	NW Ft. Sill Blvd. (Gore to Ferris) Under Construction
<b>Residential Street &amp; Drainage Improvements</b>	
Citywide Overlay & Reconstruction Projects	Phase 2 (Six Residential) Projects Under Construction/ Phase 1 (Five Residential) Projects Awarded for Construction
Greer Addition NW 35th & Arlington	Street & Drainage Project Under Construction
27th/31st St. Design (Gore to Arlington)	Project Complete
<b>Wastewater Improvements</b>	
Nine Mile Creek Sewer Line Construction	Phase II ROW Acquisition Ongoing; Ready to Bid Phase I
Alternative Water Source Feasibility Study	Draft Feasibility Report For Alternative Water Sources Submitted

**CITY OF LAWTON 2012 CIP SCHEDULE**

**ADVALOREM TAX FUNDED PROJECTS**

<b>PROJECT TYPE &amp; LOCATION</b>	<b>PROJECT STATUS</b>
<b>City Facility &amp; Other Improvements</b>	
Fire Station Improvements	Council Tabled Plans and Specifications for Fire Station #8; Ready to Bid
Landfill Maintenance Building	Council Approved Revised Plans and Specifications; Ready to Bid
Animal Welfare Facility	Project Complete

# Phase III Sewer Rehabilitation Program



- ◆ \$31 Million Funded by 2012 CIP Sales Tax
- ◆ Total Phase III Estimated \$46 Million
- ◆ Phase III (27% Complete)
- ◆ Large Line Crew – Working SE of 38<sup>th</sup> Street and Coombs Road. (48” PVC)
- ◆ Small Line Crews – Working on the Cache Creek Basin in Carriage Hills Addition.
- ◆ Working on Citywide Sewer Collapses Caused by May Flooding (7000 L.F. of 19,000 L.F. Completed at a Cost of \$1.0 Million to Date)
- ◆ Anticipated 6 to 9 Additional Months at an Estimated Cost of \$2.0 Million Remains to Repair Flooding Damage

# WWTP Improvements Work Package No 2. Project 2008-11



- ◆ Archer Western Construction, LLC
- ◆ Construction Cost \$7,157,389
- ◆ Council Approved Change Order #2 in the amount of \$371,009 Associated with HVAC, Electrical and Control System for the Sludge Blending Building at the February 10, 2015 Meeting.
- ◆ Notice to Proceed: September 1, 2013.

- ◆ Council Approved Amendment #6 in the Amount of \$84,749 With Black & Veatch to Design Modifications to the Digester Cover (Roof) at the January 27, 2015 Meeting.
- ◆ Construction 95% Complete
- ◆ Coating for Corrosion Control inside North Digester Remains

# NW 2<sup>nd</sup> Street Enhancement Phase 1-2

## Project #2014-3

### (Columbia Ave. to Ferris Ave.)



- ◆ Olsson Engineering
- ◆ Updating Original Plans to Modify Ferris and 2<sup>nd</sup> Street Intersection
- ◆ Council Approved Plans and Specifications and Authorized Staff to Advertise for Bids at Oct 27, 2015 Meeting



# SW 52<sup>nd</sup> Street (Gore to RR Tracks) Project # 2012-4 (Design)



- ◆ Garver LLC
- ◆ Design Cost \$442,000
- ◆ Council Awarded Design Contract at the July 10, 2012 Meeting.
- ◆ Final Design On-going
- ◆ Preliminary Design Report Approved
- ◆ 3-Lane Facility With 10' Bike Path Behind Curb on East Side.
- ◆ ROW Acquisition From LPS Remains (Negotiating a New Bus Drop off Location for Eisenhower Elementary Students)

# 2012 CIP Street Mill & Overlay Program

NW Fort Sill Blvd. From W. Gore Blvd. to NW Ferris Ave.  
Project #2014-4



- ◆ T&G Construction, Inc.
- ◆ Construction Cost \$1,565,742



- ◆ Notice to Proceed: March 1, 2015
- ◆ Final Inspection Remains
- ◆ Project Substantially Complete

# Local Street Reconstruction Phase 2

## Project # 2012-11



- ◆ A.E. Construction Company
- ◆ Construction Cost \$1,996,408
- ◆ Council Awarded Construction Contract at the February 24, 2015 Meeting
- ◆ Notice to Proceed: May 4, 2015
- ◆ 6 Street Reconstruction Locations Citywide

- ◆ NW 36<sup>th</sup> St (Knob Hill Ave to Kinyon Ave)
- ◆ NW 35<sup>th</sup> St (Ferris Ave to 34<sup>th</sup> St)
- ◆ SW 10<sup>th</sup> St (“B” Ave to “C” Ave) Under Construction
- ◆ SW 27<sup>th</sup> St (Lee Blvd to “J” Ave) Under Construction
- ◆ SW Summit Ave (6<sup>th</sup> St to 8<sup>th</sup> St) Under Construction
- ◆ SW “K” Ave (45<sup>th</sup> St to “K” Cir)
- ◆ 2<sup>nd</sup> and Gore Intersection Reconstruction (Project Complete)



# Local Street Reconstruction Phase 1

## Project # 2012-11



- ◆ A.E. Construction Company
- ◆ Construction Cost \$1,568,525
- ◆ Council Awarded Construction Contract at the July 14, 2015 Meeting
- ◆ Notice to Proceed: September 22, 2015
- ◆ 5 Street Reconstruction Locations Citywide

- ◆ NW Santa Fe Ave (38<sup>th</sup> St to 40<sup>th</sup> St)
- ◆ NW Lindy Ave (40<sup>th</sup> St to 46<sup>th</sup> St)
- ◆ NW 27<sup>th</sup> St (Denver Ave to Cheyenne Ave)
- ◆ NW Denver Ave (23<sup>rd</sup> St to 24<sup>th</sup> St)
- ◆ NW 24<sup>th</sup> St (Denver Ave to Cheyenne Ave)



# NW 35<sup>th</sup> Street Drainage & Street Construction Project # 2012-3 (Design)



- ◆ Council Approved Plans & Specs and Authorized Staff to Advertise for Bids at the July 22, 2014 Meeting.
- ◆ Council Approved a Construction Contract at the September 9, 2014 Meeting.


- ◆ *MTZ Construction, Inc.*
- ◆ *Construction Cost \$3,028,298*
- ◆ *Notice to Proceed: November 3, 2014*
- ◆ *Installing RCB West of 31<sup>st</sup> Street on NW Arlington.*
- ◆ *Street Completed From 25<sup>th</sup> to 31<sup>st</sup> Street on Arlington*



# Alternative Water Source Feasibility Study

## Groundwater Resources

### Minor Alluvial/ Terrace Aquifers



### Minor Bedrock Aquifers



### Major Bedrock Aquifers



### Arbuckle-Timbered Hills Aquifer


429,800 AFY available for new permits (384 MGD)

\* Current water rights permits for approx. 5,300 AFY (< 5 MGD)



- ◆ Garver, LLC
- ◆ Study Cost \$812,000
- ◆ Council Awarded Feasibility Study at the December 9, 2014 Meeting
- ◆ Draft Feasibility Report Submitted

## Indirect Potable Reuse

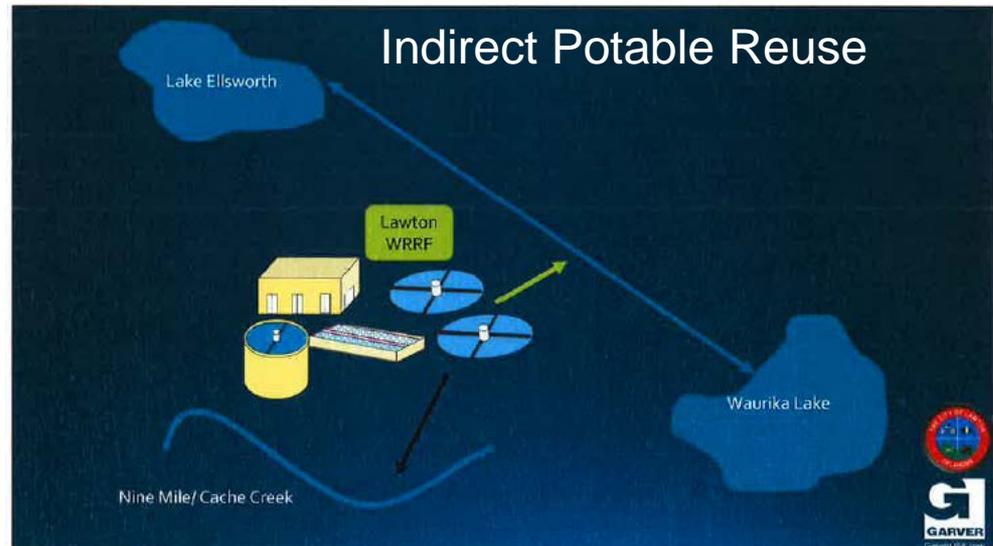

# New Fire Station #8 (Bishop Road between 52<sup>nd</sup> and 67<sup>th</sup>)




- ◆ CH Guernsey and Company
- ◆ Design Cost \$425,620
- ◆ Council Awarded Design Contract at the December 16, 2014 Meeting.
- ◆ Council Tabled Plans and Specifications to Authorize Staff to Advertise for Bids at Oct. 27, 2015 Meeting

# Landfill Equipment Maintenance Building Design Upgrade



- ◆ Bids Came in Much Higher Than the Project Budget and the Consulting Engineers Estimate.
- ◆ Plans Have Been Value Engineered to Reduce Costs and are Ready to Bid
- ◆ Council Approved Plans and Specs and Authorized Staff to Advertise for Bids at the Oct 27, 2015 Meeting

- ◆ Re2C Engineering, LLC
- ◆ Design Upgrade Cost \$49,100
- ◆ Council Rejected Bids and Authorized Staff to Revise Plans & Specs and Advertise at the November 11, 2014 Meeting.

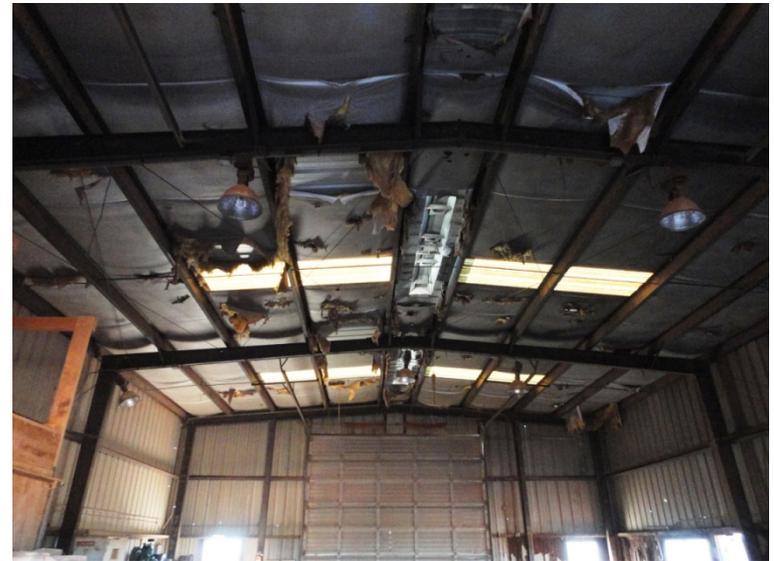

**PROPOSED TEN YEAR LAWTON 2016 CIP PACKAGE**

**SALES TAX FUNDED PROJECTS THROUGH DECEMBER 31, 2025**

<b>PROJECT TYPE &amp; LOCATION</b>	<b>PROJECT DESCRIPTION</b>	<b>FUNDING FOR REMAINING 2012 CIP PROJECTS</b>	<b>ADDITIONAL PROJECTS FOR 2016 CIP</b>	<b>TOTAL FUNDS FOR 2016 CIP</b>
<b>Mandatory Project Improvements</b>				
Phase III - Sewer Rehabilitation Program	(3/4) Citywide Trunk Mains/E. Cache Creek Basin	\$21,700,000	\$15,000,000	\$36,700,000
Landfill Cells 6 & 7 / Land Purchase	Expansion of New Cells at Landfill	\$7,500,000	\$0	\$7,500,000
		<b>\$29,200,000</b>	<b>\$15,000,000</b>	<b>\$44,200,000</b>
<b>Arterial Roadway &amp; Bridge Improvements</b>				
SE 45th St. (Lee Blvd. to Bell Ave.)	Reconstruct to (5) Lanes	\$8,500,000	\$0	\$8,500,000
		<b>\$8,500,000</b>	<b>\$0</b>	<b>\$8,500,000</b>
<b>Alternative Water Sources</b>				
Groundwater Wells	Drilling 10 Test Wells & Constructing 5 Full Wells	\$0	\$64,000,000	\$64,000,000
Groundwater Treatment Improvements	Treatment & Distribution Improvements for GW			
Reuse Water Improvements	Improvements Required to Utilize Reuse Water			
		<b>\$0</b>	<b>\$64,000,000</b>	<b>\$64,000,000</b>
<b>Residential Street &amp; Drainage Improvements</b>				
Citywide Overlay & Reconstruction Projects	50% by Ward & 50% by Priority	\$4,000,000	\$0	\$4,000,000
		<b>\$4,000,000</b>	<b>\$0</b>	<b>\$4,000,000</b>
<b>Wastewater Improvements</b>				
Nine Mile Creek Sewer Line	Construct Part of Sewer Line to Serve SE Lawton	\$8,500,000	\$0	\$8,500,000
		<b>\$8,500,000</b>	<b>\$0</b>	<b>\$8,500,000</b>
<b>LATS Transportation Improvements</b>				
Purchase Busses	Purchase New Busses for LATS	\$0	\$3,500,000	\$3,500,000
		<b>\$0</b>	<b>\$3,500,000</b>	<b>\$3,500,000</b>
<b>Total Cost of Sales Tax Improvements</b>		<b>\$50,200,000</b>	<b>\$82,500,000</b>	<b>\$132,700,000</b>

**NOTE: PROJECTS HIGHLIGHTED IN YELLOW ARE CARRIED OVER FROM THE 2012 SALES TAX**

# City of Lawton



2015 Sales Tax Extension  
*October 2015*

**PROPOSED 2015 SALES TAX EXTENSION (11 YEAR PLAN)**

Proposed Project or Equipment	Project Status	Appropriated Expenditures
<b>Public Safety</b>		
Public Safety Facility - Police, Municipal Court, and Jail Facility	Design Contract Awarded	29,600,000
Estimated Financing and Interest		2,304,186
New Fire Station 8 Additional Funding Necessary to Fully Construct Facility Including Extension of Utility Lines to Serve the Facility	Tabled Oct.27,2015; Ready to Bid	2,000,000
Demolition and Hazardous Material Mitigation of Lawton Police Department		200,000
Fire Station 1 - Remodeling and Land Acquisition for the Purpose of Expanding/Improving the Existing Central Fire Station		5,000,000
Funding for Additional Police and Fire Personnel and Compensation Adjustments	Union Negotiations On-going	29,525,000
		<b>68,629,186</b>
<b>Roadway and Bridge Improvements</b>		
Right of Way Acquisition, Utility Relocations & Reconstruction of Rogers Lane (I-44 to Village Drive) to 5 Lanes/ In Order to Match Existing Oklahoma Department of Transportation (ODOT) Funding Commitment	Environmental Assessment Submitted	4,500,000
Engineering , Right of Way Acquisition, Utility Relocation and Reconstruction of W Gore Blvd from 67th Street to 82nd Street	Design On-going	5,000,000
		<b>9,500,000</b>
<b>Public Facility Restoration</b>		
Demolition and Hazardous Material Mitigation of Wayne Gilley City Hall	Demolition Complete	40,000
Demolition and Hazardous Material Mitigation of City Hall Annex		38,000
		<b>78,000</b>
<b>Water and Sewer System Improvements</b>		
Water and Sewer Line Replacement		
Paint Water Storage Tanks	Sandblasting East Tower	
Replace Water System Pumps		
Water Monitoring System (SCADA)		
		<b>4,411,114</b>
<b>Library &amp; Recreation Improvements</b>		
Library Rehab at Main and/or Branch Locations (Upgrade Restroom and Lobby Areas, New Interior Furniture, Technology Upgrades)		808,500
Pool/Spray Park Facility, Playground/Fitness Equipment, Outdoor Walking Trail Lighting, Restore Existing Sports Facilities to Include Repair/Upgrade of McMahan Ballparks and Youth Sports Fields		2,315,000
Great Plains Museum and City Hall Annex Roof Repair/Replacement	McMahon Auditorium and Great Plains Museum Roofs – Contract Awarded	1,333,200
McMahon Auditorium HVAC Improvements and Roof Repair/Replacement		200,000
Youth Programs		
		<b>4,656,700</b>
<b>Americans with Disabilities Act (ADA) Compliance</b>		
City Wide Priorities for Removal of Barriers Faced by the Disabled, as Required by Federal Lawsuit		1,000,000
		<b>1,000,000</b>
<b>Lawton Public Schools</b>		
Window and Entry Upgrades, Playground and Fencing Upgrades at Elementary Schools, Fencing Replacement at Secondary School Grounds, Remote Entry Systems in Secondary Schools. Building Upgrades and Repairs on HVAC	Upgrades and Improvements On-going	12,500,000
		<b>12,500,000</b>
<b>Neighborhood Services</b>		
Funding for Revolving Account to Demolish Dilapidated Houses		150,000
		<b>150,000</b>
	<b>Total Cost of Sales Tax Improvements</b>	<b>100,925,000</b>

# Public Safety Facility

## Police and Jail, Municipal Court, Fire Facility

### Project # 2014-06



◆ Police Station  
& Jail



◆ Municipal Court

- ◆ Council Approved an Agreement in the Amount of \$2,872,642 with Dewberry for Professional Engineering Services to Design the Public Safety Facility at the Oct 27, 2015 Meeting



◆ Fire Station

# New Fire Station #8 (Bishop Road between 52<sup>nd</sup> and 67<sup>th</sup>) Project # 2013-11



- ◆ Council Tabled Plans and Specs to Authorize Staff to Advertise for Bids at the Oct 27, 2015 Meeting

# Rogers Lane (I-44 to Village Drive)



- ◆ Council Executed a Project Agreement with ODOT for 75% Construction Costs up to a Maximum of \$5.8 Million at the April 23, 2013 Meeting
- ◆ ODOT Submitted a Draft Environmental Clearance Document to the City for Review and Comments
- ◆ Awaiting ODOT Approval for Right of Way Acquisition to Begin
- ◆ Utility Relocations & Reconstruction of Rogers Lane to 5 Lanes

# W. Gore Boulevard Project # 2000-27 (67<sup>th</sup> to 82<sup>nd</sup>)



- ◆ Consultant : Dewberry
- ◆ Design Cost: \$ 427,100
- ◆ Design – Plans/Specifications:  
5-Lane Roadway
- ◆ Joint ODOT Project
- ◆ Design On-going



# Demolition of Wayne Gilley City Hall



- ◆ Demolition Complete
- ◆ Final Cleanup Complete




# Tower Repainting Project # 2015-06



◆ East High Zone Tower

- ◆ Contractor: Sherman Williams
- ◆ Construction Cost: \$793,700
- ◆ Notice to Proceed: Sept 15, 2015
- ◆ Sandblasting East Tower

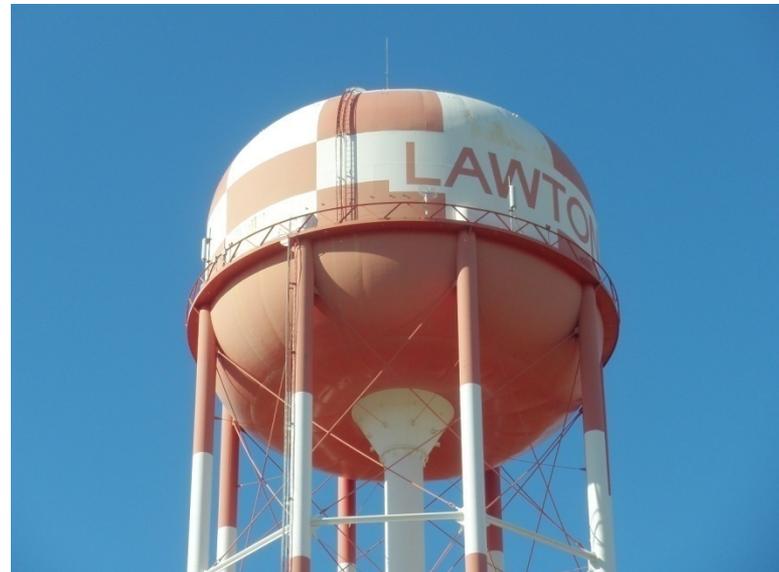

◆ West Industrial Tower

# McMahon Auditorium and Great Plains Museum Roofing Project # 2015-03



- ◆ Contractor: Ford Roofing
- ◆ Construction Costs: \$545,350
- ◆ Contract Awarded by State of Oklahoma
- ◆ Under Construction

QUESTIONS?
